



Theberton & Eastbridge Parish Council

Wednesday 22 July 2026

B1122 Early Years: Nighttime Working 1900 - 0500

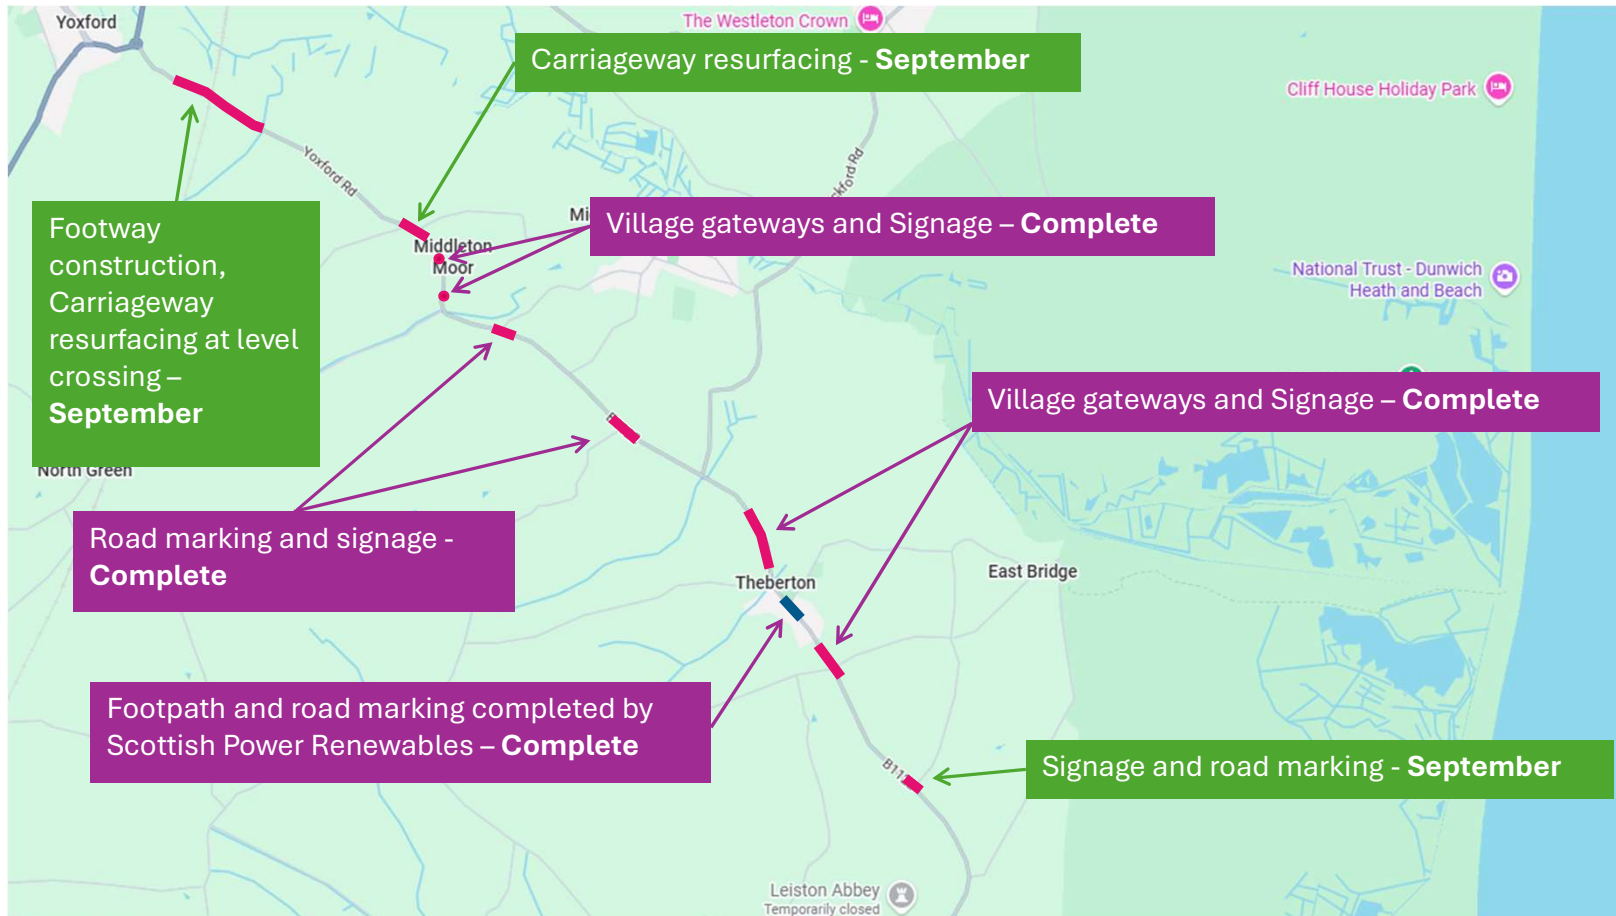

Road Closures (SLR Summary): From 10 August

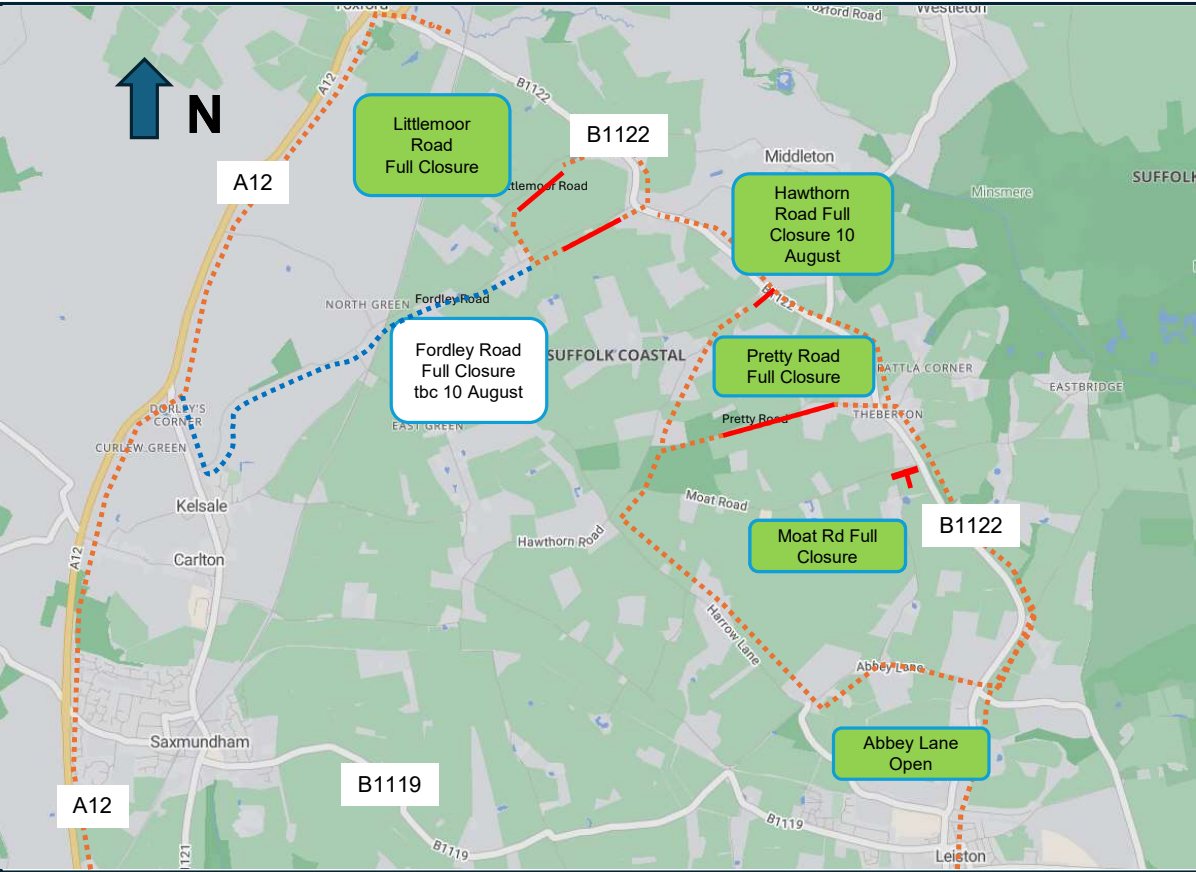

Legend:

Road Closure



Diversion



Approved




In process



Road Closure – November 2026 to March 2027


Current Road Closure Programme

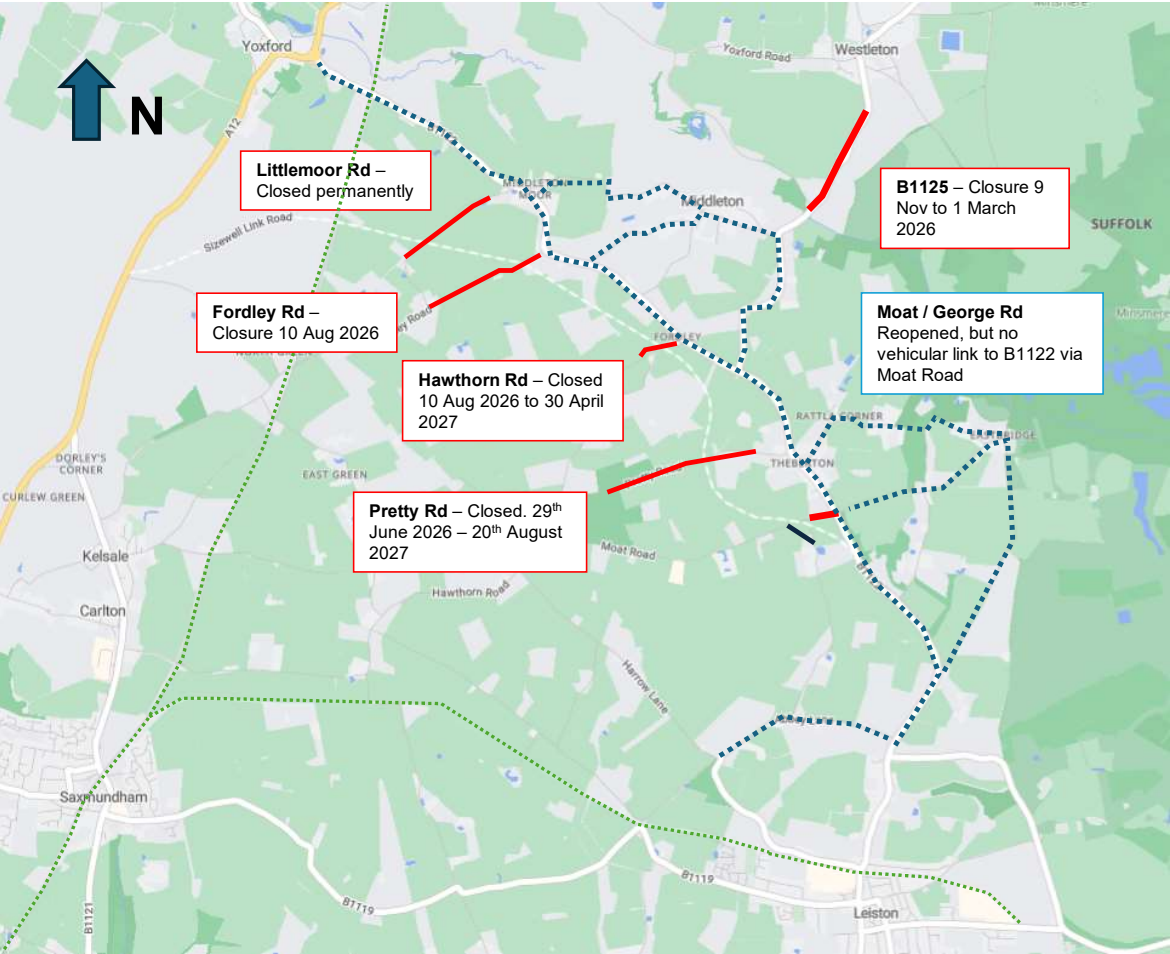

Legend:

- Road Closure
- B1122 Open Roads

Main Development Site Roads: Scheme Summary

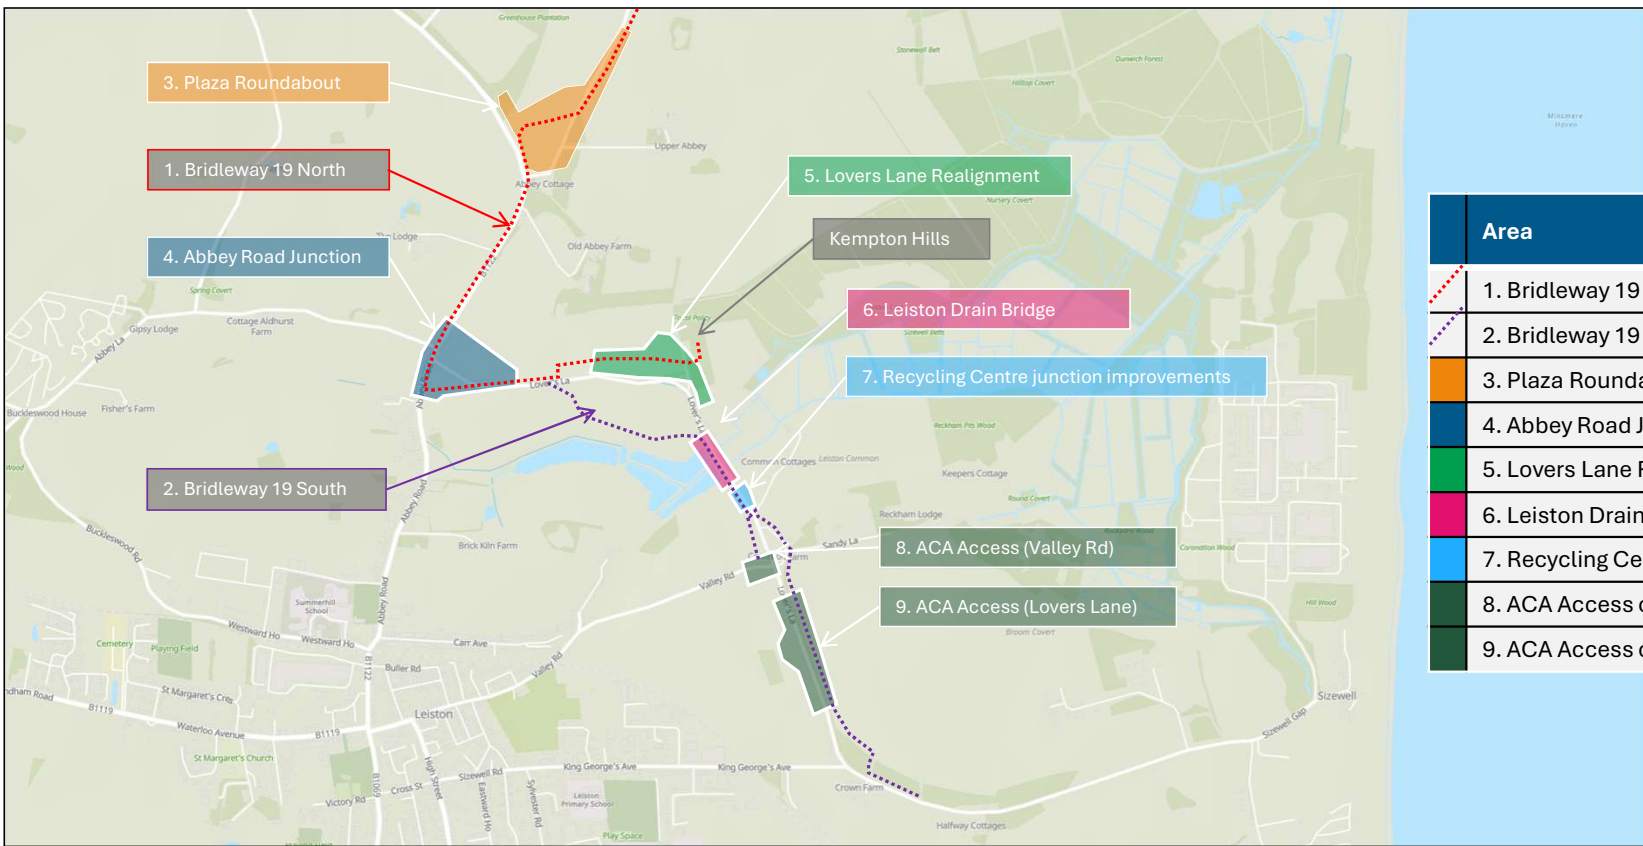

	Area	Completion Date
	1. Bridleway 19 North	Q4 2026
	2. Bridleway 19 South	Q2 2027
	3. Plaza Roundabout	Q4 2026
	4. Abbey Road Junction	Q4 2026
	5. Lovers Lane Realignment	Q3 2026
	6. Leiston Drain Bridge	Q2 2027
	7. Recycling Centre	Q1 2027
	8. ACA Access off Valley Road	Q1 2027
	9. ACA Access off Lovers Lane	Q1 2027

MDS Road Closure Programme Q3/Q4 2026

Road Closures to Enable Completion of Plaza Roundabout and Abbey Road

Closure No.	Description	Start - End	Extents	Scope	Supporting Narrative	Ref
1	Weekend Closure	20:00 Fri 04/09 - 05:00 Mon 07/09	Lovers Lane Only	Kenton Hills	Planing of Kenton Hills. Removal of Defective Area. Surface Course.	692
2	4no. Weekday Nights	20:00 - 05:00 Mon 07/09 - Fri 11/09	Lovers Lane Only	Surface Course	Surface Course for SAR, Lovers Lane, Kenton Hills. Removal of old road, surfacing at crossing. Anti Skid.	709
3	Weekend Closure	20:00 Fri 11/09 - 05:00 Mon 14/09	Full MDS (Rowley Mews, Potters Street, Sandy Lane)	Plaza Roundabout South Tie In (1)	Plaza Tie In (South - Week One).	691
4	Weekend Closure	20:00 Fri 18/09 - 05:00 Mon 21/09	Full MDS (Rowley Mews, Potters Street, Sandy Lane)	Plaza Roundabout Contingency	Booked - This is a contingency for the Plaza.	698
5	Weekend Closure	20:00 Fri 25/09 - 05:00 Mon 28/09	Full MDS (Rowley Mews, Potters Street, Sandy Lane)	Plaza Roundabout South Tie In (2) Rowley Mews	Plaza Tie In (South - Week Two). Temporary Works / Alignment at RM.	693
6	Weekend Closure	20:00 Fri 02/10 - 05:00 Mon 05/10	Full MDS (Rowley Mews, Potters Street, KGA)	Plaza Roundabout Contingency Rowley Mews	Booked - This is a contingency for the plaza. However, plan to surface course Abbey Road / Rowley Mews, including kerb replacement, lighting, and Anti Skid.	694
7	Weekend Closure	20:00 Fri 09/10 - 05:00 Mon 12/10	Full MDS (Rowley Mews, Potters Street, KGA)	Plaza Roundabout North Tie In (1) Rowley Mews	Plaza Tie In (North - Week One).	700
8	Continuous Closure	20:00 Fri 09/10 - 05:00 Mon 26/10	Eastbridge Road	Eastbridge Road Tie In	Eastbridge Full Closure to enable tie in of New Eastbridge Road Leg between two weekend closure.	711
9	Weekend Closure	20:00 Fri 16/10 - 05:00 Mon 19/10	Full MDS (Rowley Mews, Potters Street, KGA)	Plaza Roundabout Contingency	Contingency.	695
10	Weekend Closure	20:00 Fri 23/10 - 05:00 Mon 26/10	Full MDS (Rowley Mews, Potters Street, KGA)	Plaza Roundabout North Tie In (2) Rowley Mews	Plaza Tie In (North - Week Two), including Traffic Switch.	696
11	4no. Weekday Nights	20:00 - 05:00, Mon 26/09 - Fri 30/10	Full MDS (Rowley Mews, Potters Street, KGA)	Plaza Roundabout Contingency	Surface Course of Plaza Roundabout. Street Lighting. Signage. Anti Skid.	710
12	Weekend Closure	20:00 Fri 13/11 – 05:00 Mon 16/11	Lovers Lane Only	Contaminated Land Carriageway	Lovers Lane (Western Tie-In) Full-Depth Reconstruction. Mammal Crossing. Planing of Kenton Hills. Base & Binder. Removal of Defective Area.	XXX
